Northampton Township
55 Township Road
Richboro, Pa 18954
Zoning-Code Enforcement Department
Phone #: 215-355-3883
Fax #: 215-357-3650

Right-of-Way/Road Occupancy – Permit Application

Job Location: _____

Owner Name _____ Phone No.: _____

Applicant Name (print): _____ Phone No.: _____

Address: _____

Signature: _____ Date: _____

If applicant is a contractor, please provide HIC # _____

Description of Proposed Work: _____

_____

APPLICANT MUST SUPPLY THE FOLLOWING INFORMATION:

1.	**Will the roadway surface be opened?**	**Yes** _____ **No** _____
2.	**Will the job require boring under the roadway?**	**Yes** _____ **No** _____
3.	Number of working days to complete work:	
4.	Approximate area of road opening:	sq. yds.
5.	Approximate area of unimproved right-of-way to be disturbed	sq. yds.
6.	Length of trench along improved roadway:	ft.
7.	Length of trench along unimproved right-a-way:	ft.
8.	Depth of trench:	Inches
9.	Diameter of pipe to be placed:	Inches
10.	Number of poles to be erected:	
11.	Amount of sidewalk to be removed and replaced:	sq. ft.
12.	Amount of curb to be replaced:	linear ft.

Any permit issued will be under; and subject to, the conditions, restrictions and regulations of PennDot Publication 408 (where applicable), all applicable Township Ordinance and specifications included with each application.

All work shall be subject to inspection by the Township Engineer, CKS Engineers at 215-340-0600. Minimum notice of 48 hours shall be provided.

Township Right of Way / Road Occupancy Diagram

Location of Proposed Work: _____

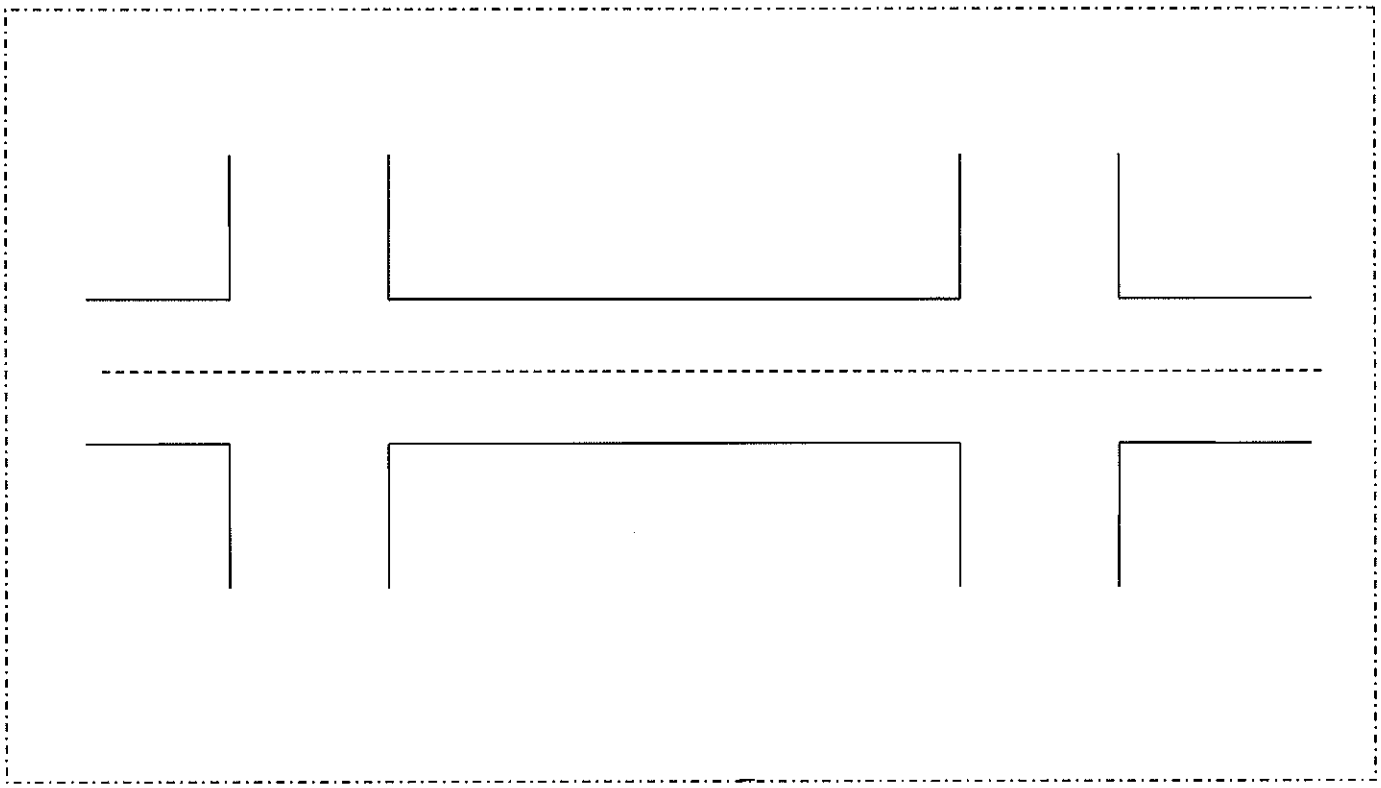

Notes:

1. Permittee to show all dimensions.
2. Permittee to show all curb, sidewalk, storm sewer, swales and driveways.
3. Permittee to show all proposed improvements including widths, pipe sizes and trench locations.
4. Permittee to show any pertinent information such as road widths, obstruction or unusual situations.
5. Driveway pipes to be minimum 18 inch diameter and are to extend at least one foot beyond each side of driveway.
6. Swales to conform to present ditch line, so as not to restrict flow of surface water.
7. Temporary pavement restoration to be completed at the end of each work day.
8. Permanent restoration (roadway and unimproved area) to be completed within 60 days.

Ref. No. 2876

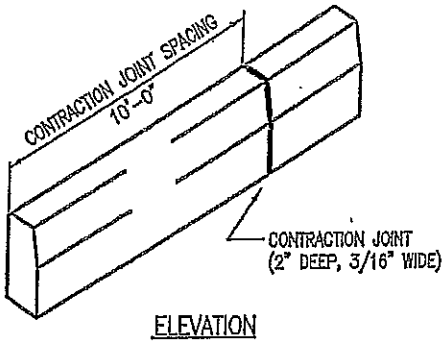

ELEVATION

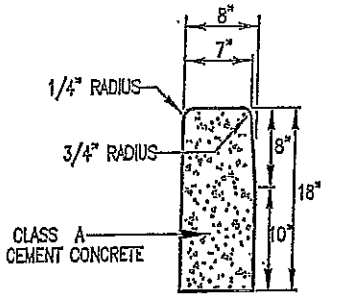

TYPICAL CROSS SECTION

PLAIN CEMENT CONCRETE CURB

N.T.S.



DEPRESSED CURB

N.T.S.

NOTE:
ROADWAY AND RIGHT-OF-WAY RESTORATION AS PER RESTORATION DETAILS ENCLOSED.

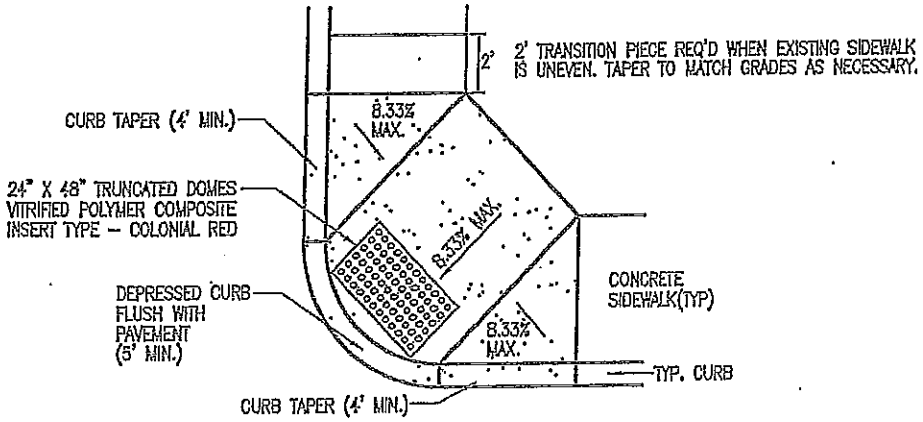

DETAIL - HANDICAP RAMP

N.T.S.

NOTE:
ALL HANDICAP RAMP CONSTRUCTION TO MEET ALL APPLICABLE ADA REQUIREMENTS.



NOTES:
1. NON-SLIP BROOM FINISH SHALL BE PROVIDED ON ALL PEDESTRIAN PAVEMENTS. ALL EXTERIOR CONCRETE SHALL BE AIR ENTRAINED AND HAVE A MINIMUM COMPRESSIVE STRESS OF 3300 PSI (CLASS A).
2. STANDARD SIDEWALK TO BE MIN. 4 INCHES CONCRETE.
CONCRETE DRIVEWAY APRONS TO BE MIN. 6 INCHES CONCRETE W/ 6 X 6 WIRE MESH.

CONCRETE SIDEWALK DETAIL

N.T.S.

Northampton Township, Bucks County, Pennsylvania

CKS Engineers, Inc.
88 South Main Street, Doylestown, PA 18901
(215) 340-0600

C:/ACAD/TOWNSHIP/NORTHAMPTON/2876/2876_Permit_Plan.DWG*TNS

NORTHAMPTON TOWNSHIP, BUCKS COUNTY, PA
FINAL CARTWAY TRENCH RESTORATION

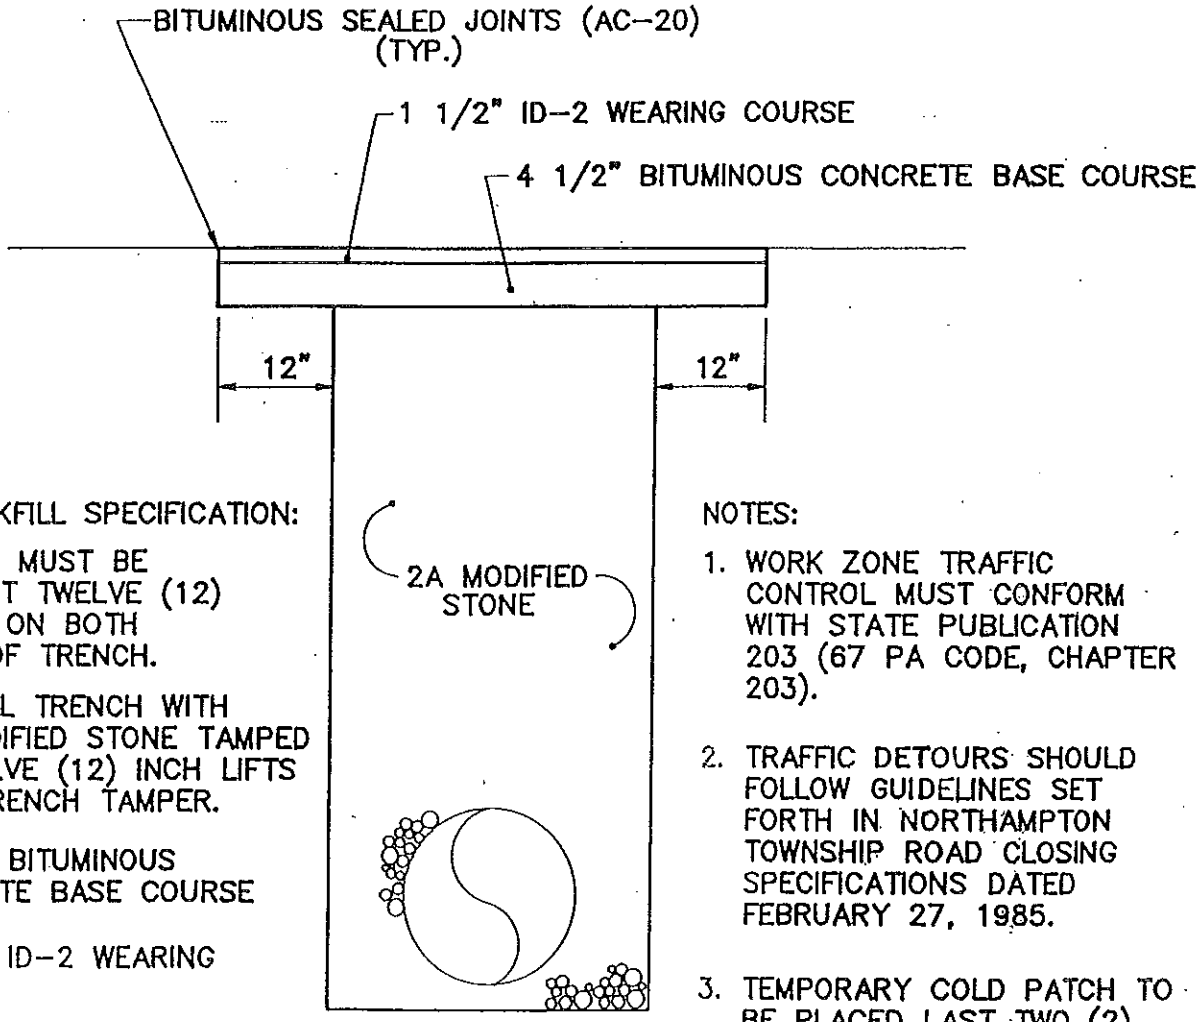

FINAL BACKFILL SPECIFICATION:

1. TRENCH MUST BE OVERCUT TWELVE (12) INCHES ON BOTH SIDES OF TRENCH.
2. BACKFILL TRENCH WITH 2A MODIFIED STONE TAMPED IN TWELVE (12) INCH LIFTS WITH TRENCH TAMPER.
3. 4 1/2" BITUMINOUS CONCRETE BASE COURSE
4. 1 1/2" ID-2 WEARING COURSE
5. ALL JOINTS SEALED WITH AC-20 ASPHALT CEMENT

NOTES:

1. WORK ZONE TRAFFIC CONTROL MUST CONFORM WITH STATE PUBLICATION 203 (67 PA CODE, CHAPTER 203).
2. TRAFFIC DETOURS SHOULD FOLLOW GUIDELINES SET FORTH IN NORTHAMPTON TOWNSHIP ROAD CLOSING SPECIFICATIONS DATED FEBRUARY 27, 1985.
3. TEMPORARY COLD PATCH TO BE PLACED LAST TWO (2) INCHES FROM TOP OF TRENCH PRIOR TO FINAL RESTORATION.
4. APPLICANT WILL BE RESPONSIBLE FOR MAINTENANCE OF TEMPORARY RESTORATION.
5. CONTACT THE PUBLIC WORKS DEPARTMENT TWO (2) DAYS PRIOR TO START OF WORK AT 355-3433.

C K S Engineers, Inc.
88 South Main Street, Doylestown, PA 18901
(215) 340-0600

August, 1996
